

Chemung County Stormwater
Construction Inspection
Erosion and Sediment Control

Project Name <u>Red Robin</u>	Date <u>6/16/2014</u>
Location <u>So. Tier Crossing</u>	Permit # <u>NYR10J873</u>
Weather Conditions <u>sunny</u>	Entry Time: <u>9:00</u>
On-Site Representative Present: <u>Raymond Miles</u>	Exit Time: <u>9:20</u>

Sketch of Project site-Include Disturbed Areas:

- Construction entrance has been re-topped - looks good

Yes	No	N/A	
X			All erosion and sediment control measures installed/constructed
	X		All erosion and sediment control measures maintained properly
	X		Are there currently more than 5 acres disturbed w/o prior approval
		X	Have stabilization measures been initiated in inactive areas
	X		Are permanent stormwater control measures being implemented
	X		Was there a discharge into the receiving water on the day of inspection
	X		Evidence of turbidity or oil in the receiving waters
X			Are weekly inspections being performed?
X			Are the inspections being performed by a qualified individual?

needs inlet protection maint.

Comments:

#1 - ^{Both} Drop inlet protection - ~~at~~ ~~entrance~~ requires maintenance - replace fabric - there are holes

Note - concrete washout is near capacity

Satisfactory Marginal Unsatisfactory

Date <u>6/16/14</u>	Inspector <u>Josua Verrigni</u>
---------------------	---------------------------------

Repair drop inlet protection. Site looks good



851 Chemung Street
Horseheads, New York 14845
Ph. 607.796.2216

PROJECT:	Red Robin
	Town of Horseheads
	Municipal Inspection
	June 16, 2014

BY	Jessica Verrigni, CPESC, CPSWQ
-----------	--------------------------------




Construction entrance was recently re-topped with fresh stone.



Drop inlet protection has holes and needs to be replaced.



Concrete washout is near capacity and needs maintenance soon.

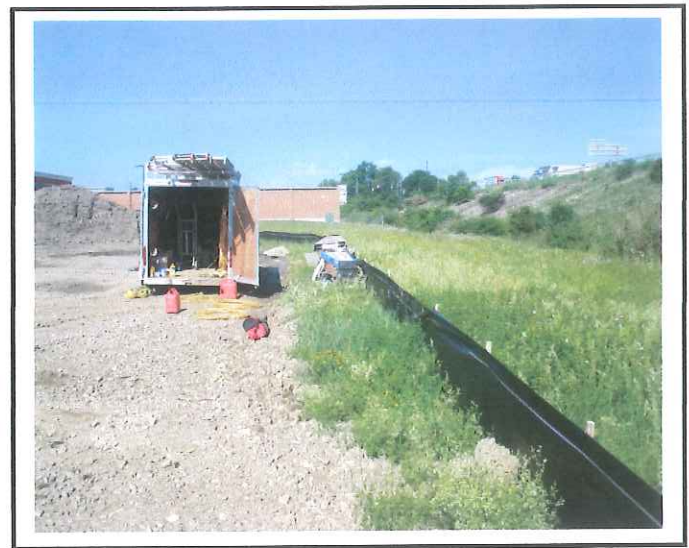

Silt fence maintained between project and stormwater swale.
